


Dworshak Unit 3 List of Milestones with complimentary Generator Diagram

Diagram was taken from: https://en.m.wikipedia.org/wiki/Water_turbine on 21 SEP 2016

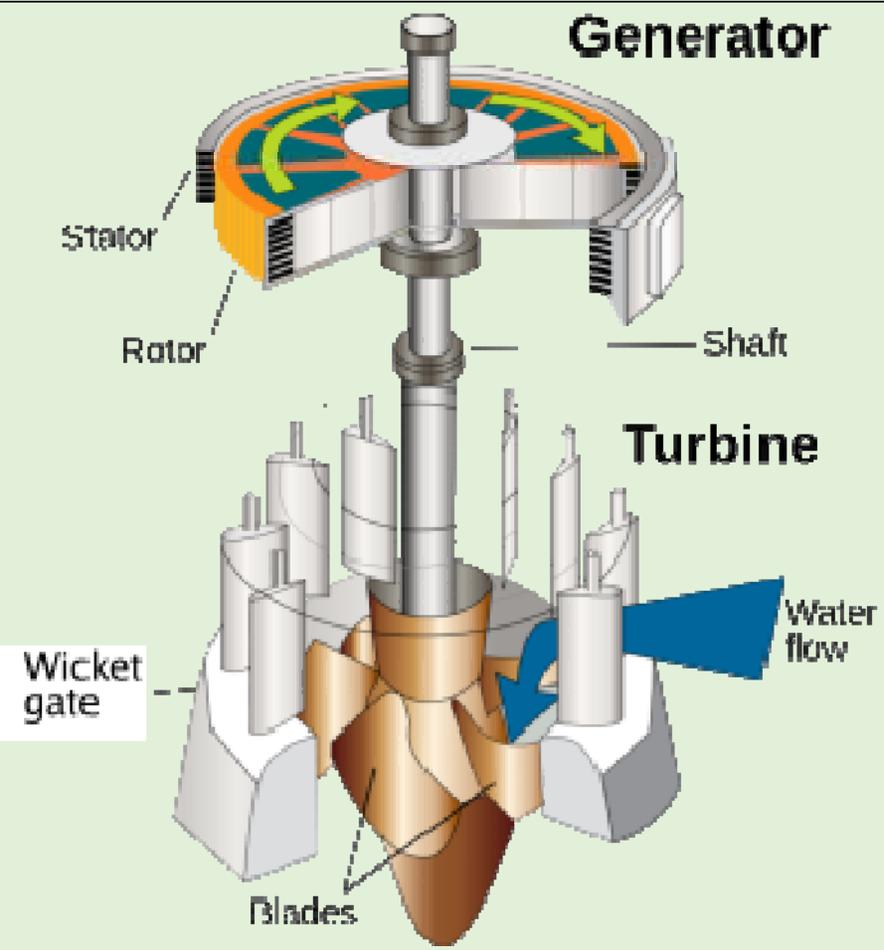

- ✓ Generator Disassembly Start 19 Sep 2016
 - ❑ Rotor Removed 11 Oct 2016
 - ❑ Winding Removal Complete 29 Oct 2016
 - ❑ Stator Core Removal Complete 05 Nov 2016
-
- ❑ Install Stator Core Complete 08 Dec 2016
 - ❑ Rotor Work Complete 24 Jan 2017
 - ❑ Winding Install Complete 11 Mar 2017
 - ❑ Unit Reassembly Complete 05 Apr 2017
 - ❑ U3 RTS 01 May 2017.
 - ❑ Special Field Tests Completion 15 May 2017
 - ❑ Model Validation Testing completion 01 July 2017.
